

CITY COUNCIL

For City Clerk's Use:

☐ **APPROVED** ☐ **DENIED**

Reso No. _____ File No. _____

Ord No. _____

Agenda Item No.: 9

Date: June 20, 2012

TO: Honorable Mayor and Members of the City Council

FROM: Edward N. Domingue, Director of Engineering Services
Dan Higbee, Acting Construction Project Manager

SUBJECT: Notice of Completion for Ash Street Pedestrian Bike Path Project

RECOMMENDATION:

It is requested that Council approve and accept the public improvements and authorize staff to file a Notice of Completion for the Ash Street Pedestrian Bike Path Project.

FISCAL ANALYSIS:

Total project cost was \$1,770,726.54. Funding was provided from a SANDAG grant and Local Transnet funds.


PREVIOUS ACTION:

On April 28, 2010, Council approved Resolution No. 2010-55 accepting SANDAG grant funds for this project. On August 10, 2011, Council awarded Southland Paving, Inc. the Ash Street Pedestrian Bike Path Project for \$2,042,983.


BACKGROUND:

The Ash Street Pedestrian Bike Path Project consists of improvements to the existing bike path, addition of underbridge crossing, colored reinforced retaining walls, wall graphics, storm drain, street lights, landscaping, underbridge lighting, fencing, paving, and striping. Project revisions to minimize impacts to the Escondido Creek Channel and optimize construction methods resulted in the final project expenses being less than the original construction bid.

Respectfully submitted,




Edward N. Domingue, P.E.
Director of Engineering Services



Dan Higbee
Acting Construction Project Manager

ASH STREET PEDESTRIAN BIKE PATH PROJECT

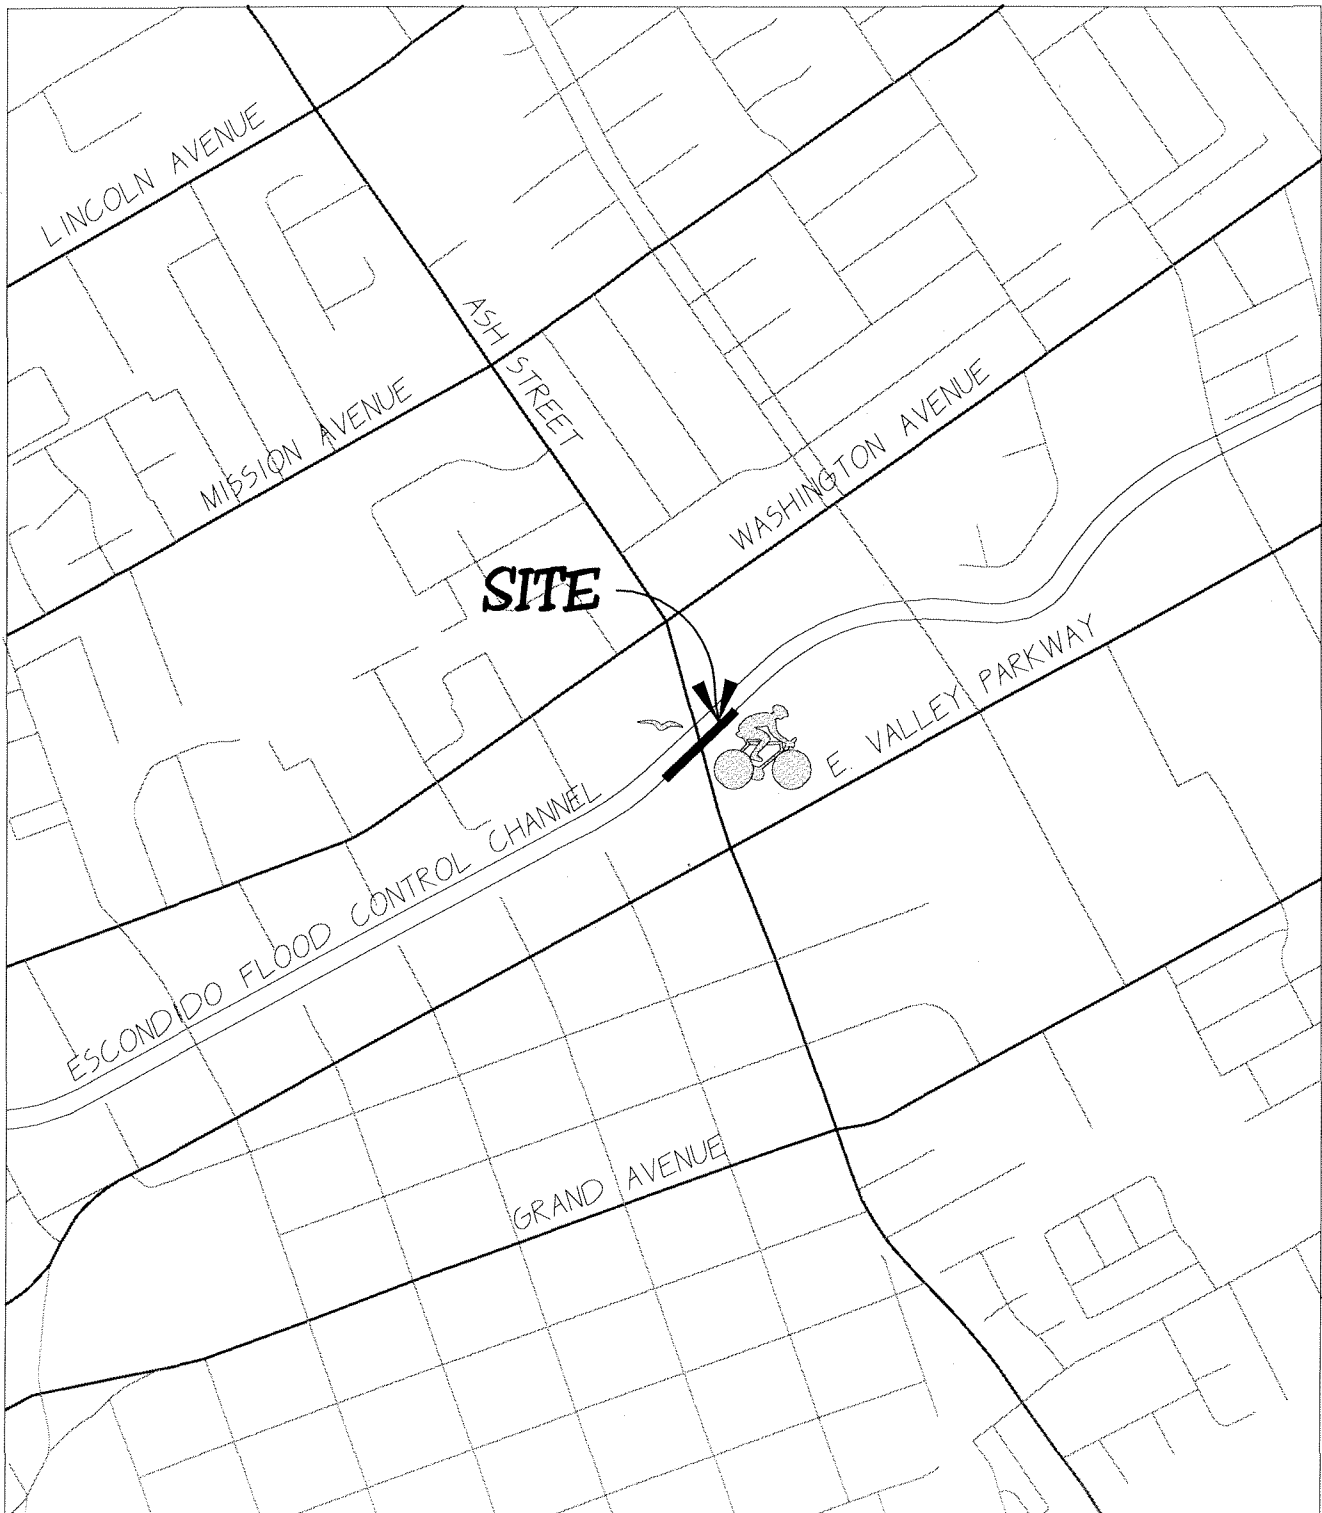

NOTICE OF COMPLETION
CITY COUNCIL MEETING 06-20-2012

